ID	Task Name	Duration	Start	Finish
1				
2				
3	**Autzen Stadium East videoboard Project Schedule**	**114 days**	**Thu 4/3/14**	**Sat 9/6/14**
4	Bid posting and response	5 days	Thu 4/3/14	Wed 4/9/14
5	Bid review	3 days	Thu 4/10/14	Mon 4/14/14
6	Letter of Intent	2 days	Tue 4/15/14	Wed 4/16/14
7	Contract issued	7 days	Thu 4/17/14	Fri 4/25/14
8				
9	**Project Coordination / Services**	**13 days**	**Thu 4/17/14**	**Mon 5/5/14**
10	Preliminary Designs	3 days	Thu 4/17/14	Mon 4/21/14
11	Submittal Drawings	5 days	Tue 4/22/14	Mon 4/28/14
12	Submittal to Client / Client Review	5 days	Tue 4/29/14	Mon 5/5/14
13				
14	**Manufacturing**	**40 days**	**Mon 4/28/14**	**Fri 6/20/14**
15	LED Product	40 days	Mon 4/28/14	Fri 6/20/14
16				
17	**Shipping**	**20 days**	**Mon 6/23/14**	**Fri 7/18/14**
18	LED Product	20 days	Mon 6/23/14	Fri 7/18/14
19				
20	**Installation**	**40 days**	**Thu 6/12/14**	**Wed 8/6/14**
30				
31	**Electrical**	**26 days**	**Thu 6/26/14**	**Thu 7/31/14**
37				
38	**Commissioning**	**28 days**	**Fri 8/1/14**	**Sat 9/6/14**
39	Start Up & Testing	2 days	Fri 8/1/14	Mon 8/4/14
40	Operator Training	2 days	Tue 8/5/14	Wed 8/6/14
41	Event Support	1 day	Sat 8/30/14	Sat 8/30/14
42	Event Support	1 day	Sat 9/6/14	Sat 9/6/14

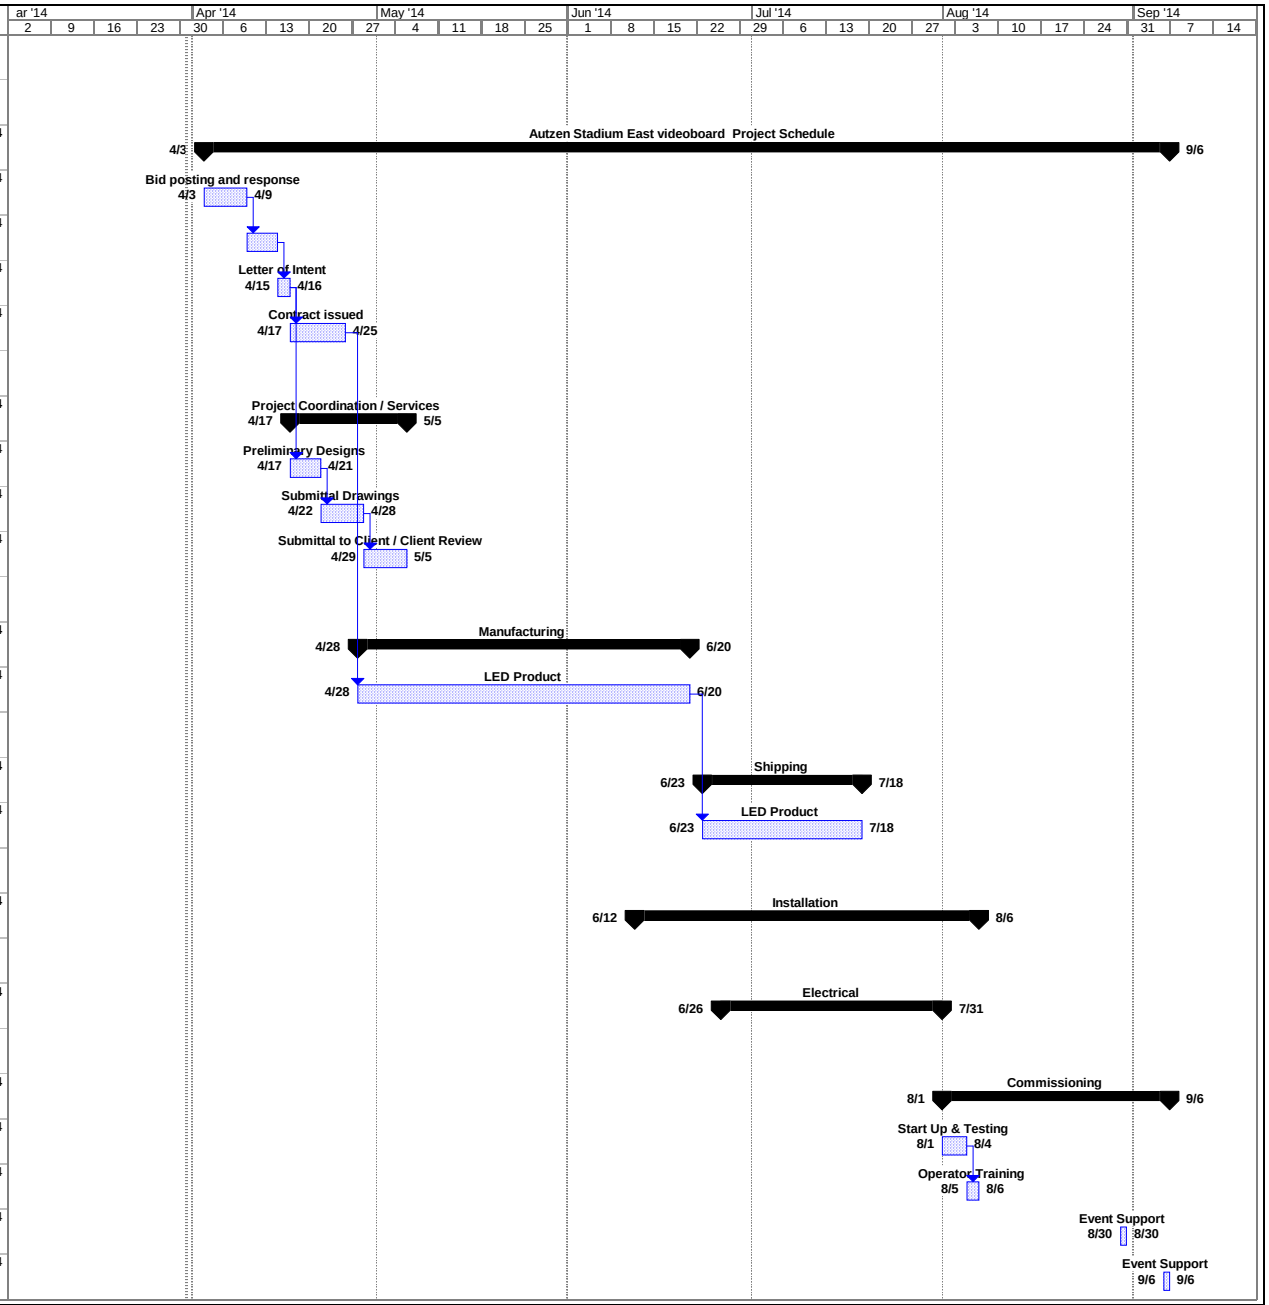

Project: MSProj11
Date: Mon 3/31/14

Task | Milestone | Project Summary | External Milestone | Inactive Milestone | Deadline
Split | Summary | External Tasks | Inactive Task | Progress

Exhibit C - AD2014-9 Autzen Stadium Video Board Display
