SBA EXPANSION & RENOVATION

Thu 5/15/14

ID	Task Name	Duration	Start	Finish	Predecessors
1	**A&E and CM/GC Procurement**	**138 days**	**Mon 7/1/13**	**Wed 1/8/14**	
24	**Design**	**381 days**	**Thu 1/9/14**	**Thu 6/25/15**	
25	Programming	95 days	Thu 1/9/14	Wed 5/21/14	14
26	Programming Cost Estimate Due	0 days	Fri 5/30/14	Fri 5/30/14	25FS+7 days
27	PSU Review & Approval of Cost Estimate	9 days	Mon 6/2/14	Thu 6/12/14	26
28	Schematic Design	55 days	Fri 6/13/14	Thu 8/28/14	27
29	Schematic Design Cost Estimate Due	0 days	Thu 9/11/14	Thu 9/11/14	28FS+1(days
30	PSU Review & Approval of Cost Estimate	10 days	Fri 9/12/14	Thu 9/25/14	29
31	Design Development	66 days	Fri 9/26/14	Fri 12/26/14	30
32	Design Review - City of Portland	66 days	Fri 9/26/14	Fri 12/26/14	30
33	Design Development Cost Estimate Due	0 days	Tue 1/6/15	Tue 1/6/15	31FS+7 days
34	PSU Review & Approval of Cost Estimate	10 days	Wed 1/7/15	Tue 1/20/15	33
35	Construction Documents	92 days	Wed 1/21/15	Thu 5/28/15	34,32
36	BP1 - Utility Relocations & Demo	67 days	Mon 12/29/14	Tue 3/31/15	31
37	BP2 -Cladding	50 days	Fri 11/21/14	Thu 1/29/15	34FS-43 days
38	Construction Documents Cost Estimate Due	0 days	Thu 6/25/15	Thu 6/25/15	35FS+2(days
39	**Construction**	**630 days**	**Fri 1/30/15**	**Thu 6/29/17**	
40	BP1 - Utilities Relocation & Demo - Permitting	65 days	Wed 4/1/15	Tue 6/30/15	36
41	BP1 - Utilities Relocation & Demo - Bidding	20 days	Wed 4/1/15	Tue 4/28/15	36
42	BP1 - Utilities Relocation & Demo - Contracting	30 days	Wed 4/29/15	Tue 6/9/15	41
43	BP1 - Utility Relocations & Demo	64 days	Wed 7/1/15	Mon 9/28/15	42,40
44	BP2 - Cladding - Bidding	20 days	Fri 1/30/15	Thu 2/26/15	37
45	BP2 - Cladding Contracting	23 days	Fri 2/27/15	Tue 3/31/15	44
46	BP2 - Cladding Lead Time	131 days	Wed 4/1/15	Wed 9/30/15	45
47	Bidding - Expansion and Renovation	20 days	Fri 5/29/15	Thu 6/25/15	35
48	Permitting	88 days	Fri 5/29/15	Tue 9/29/15	35
49	Contract GMP	45 days	Fri 6/26/15	Thu 8/27/15	47
50	Construct New Expansion	392 days	Wed 9/30/15	Thu 3/30/17	49,48,43
51	Renovate Old GSE Space	218 days	Tue 9/1/15	Thu 6/30/16	49,46FS- days
52	Reclad West	88	Thu 10/1/15	Mon 2/1/16	46
53	Renovate Old SBA Space	239 days	Fri 7/1/16	Wed 5/31/17	51
54	Reclad East	88	Mon 8/1/16	Wed 11/30/16	53SS+21
55	Atrium Demolition	88	Mon 8/1/16	Wed 11/30/16	53SS+21
56	Commissioning	300 days	Fri 5/6/16	Thu 6/29/17	51FS-40 days

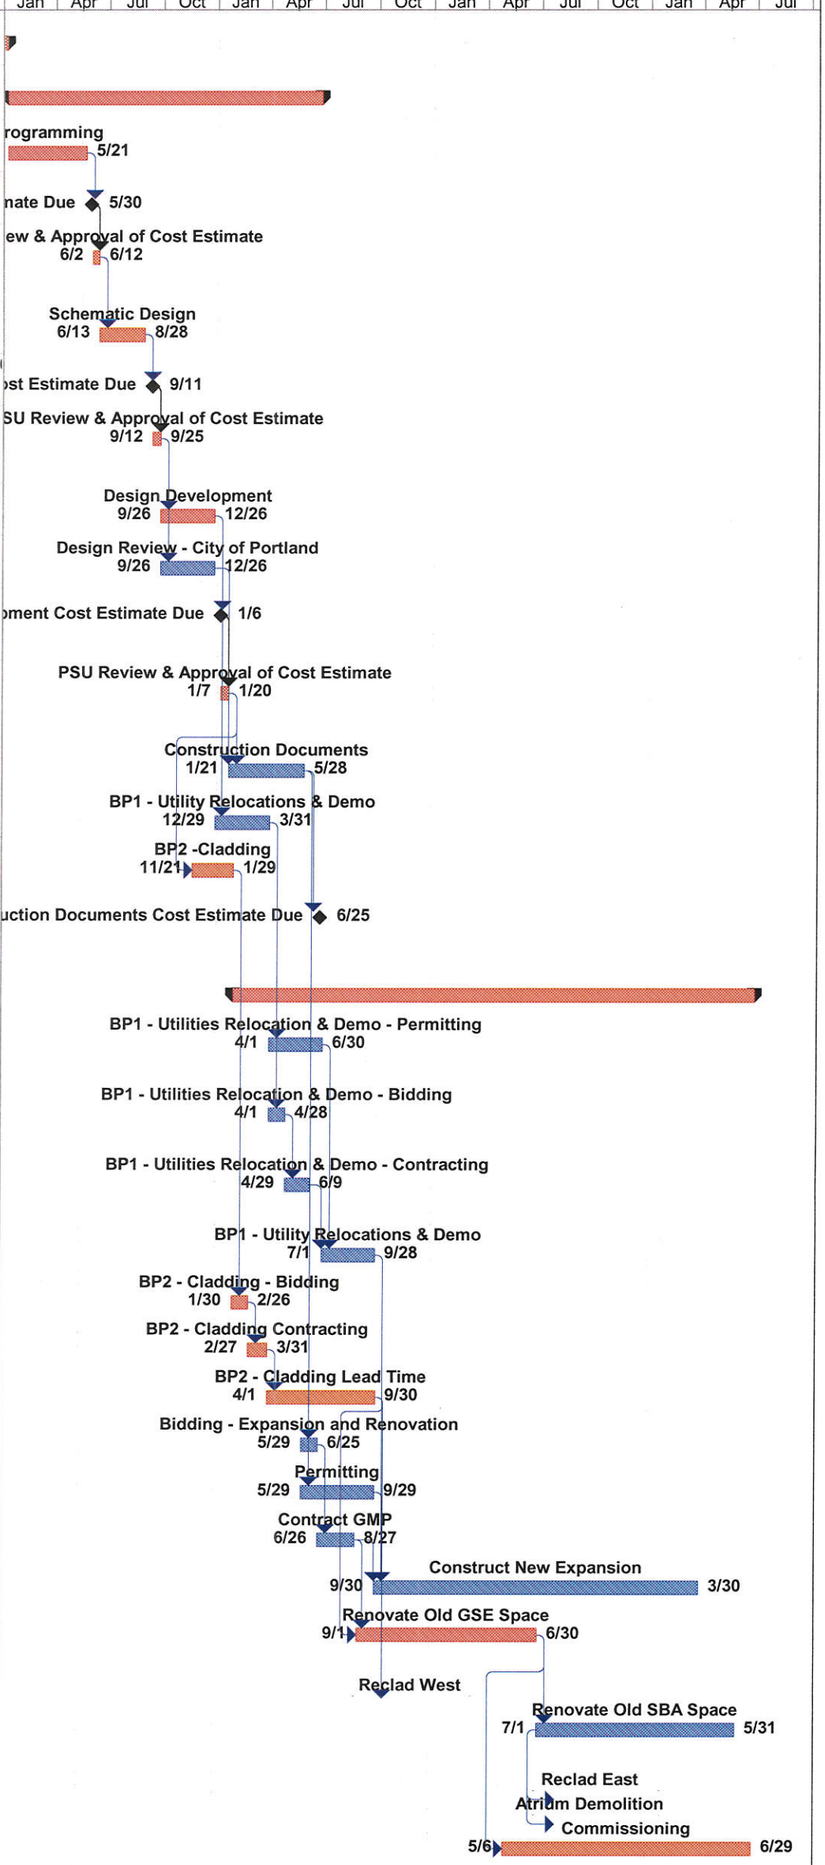

Project: SBA Expansion Project Sched
Date: Thu 5/15/14

Task	Inactive Task	Start-only	
Split	Inactive Milestone	Finish-only	
Milestone	Inactive Milestone	External Tasks	
Summary	Inactive Summary	External Milestone	
Project Summary	Manual Task	Progress	
External Tasks	Duration-only	Deadline	
External Milestone	Manual Summary Rollup		
Tasks	Manual Summary		
